



16th DELPHI Dismantling Meeting

Monday, 26 March 2001, 8:15 h

Progress during week 12/2001

Planning for week 13/2001

A.O.B

Progress during last week (week 12/2001)



Task Name	18 Mar '01						25 Mar '01			
	S	M	T	W	T	F	S	S	M	
dismantling thick endcap		[Blue hatched bar]								[Blue hatched bar]
extraction of chambers		[Blue hatched bar]						[Blue hatched bar]		
lift to SX		[Blue hatched bar]								[Blue hatched bar]
finish clean-up of barrel (A, lower half)		[Blue vertical lines bar]								
removal of cables between Barrel and D1,D2				[Blue vertical lines bar]						
removal of cryo equipment from D3		[Pink vertical lines bar]								

to continue
To continue

Good progress. No major problems, but...




Minor problems during week 12:

- no emptying of skips !
J&B / Serbeco had forgotten DELPHI .
- Portique in Peney does not allow longitudinal displacement.

Limited capacity for unloading and cutting:
2 small modules (ca. 30 T) or 1 large module (70 T).

Expect some delays this week.

Start with dismantling of
counting houses
instead of EC A.

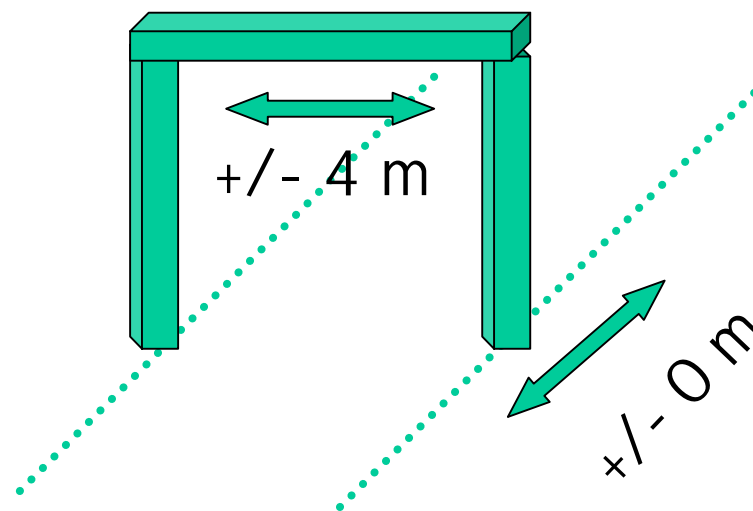

Transports foreseen for week 13.



Par ST/HM:

Lundi: 1 transport. Point 8 (DELPHI) -> Peney. 2 secteurs EC lourd. 2 x 27 T.

Mardi: 1 transport. Point 6 (OPAL) -> Peney. 1 module 70T.

Mercredi: 1 transport. Point 8 (DELPHI) -> Peney. 2 secteurs EC lourd. 2 x 27 T.

Mardi: 1 transport. Point 6 (OPAL) -> Peney. 1 module 70T. Groupe 3.

Vendredi: 1 transport. Point 8 (DELPHI) -> Peney. 2 secteurs EC lourd. 2 x 27 T.

Bennes:

1 x 9 m3 (INOX)

1 x 30 m3 (Ferraille divers)

1 x 4 m3 (Composite)

1 x 30 m3 (Composite)

1 x 7 m3 (Alu)

Planning for this week (week 13/2001)



ID	Task Name	25 Mar '01							1 Apr '01	
		S	M	T	W	T	F	S	S	M
1	dismantle 2 base EC sectors (C)		█							
2	displace platforme C					█				
3	remove racks C3						█			
4										
5	clean up cables Barrel/D1,D2		█							
6										
7	remove cryo equipment D3		█							
