

5th DELPHI Dismantling Meeting



Monday, 8 Jan 2001, 8:15 h

Happy New Year

Progress during week 51/2000

Planning for week 02/2001

A.O.B

Progress during last week (week 51/2000)



ID	Task Name	Duration	Sun 17 Dec	Mon 18 Dec	Tue 19 Dec	Wed 20 Dec	Thu 21 Dec	Fri 22 Dec	Sat 23 Dec	Sun 24 Dec	Mon 25 Dec	Tue 26 Dec	
			S	M	T	W	T	F	S	S	M	T	
1	remove gas racks from B4	4.5 days		[blue bar]					crane men + gas team + Patrick				
2	remove electronics	4.5 days		[blue bar]					Philippe + team + det. groups				
3	prepare gas racks C3	2 days		[blue bar]		Leon, Sari							
4	prepare gas racks A3	2.5 days				[blue bar]		Sari, Leon					
5	remove passerelle B4 - Barrel	2 days				[blue bar]		Dominique, Hassaine					
6	Inspection/Closure TPC A side	2.5 days		[blue bar]			TPC team						
7	move endcap A to TX	1 day		[blue bar]	Jean, Bernard								
8	Photo endcap A	0.5 days			[blue bar]	CERN photo service							
9	move endcap A to garage	0.5 days			[blue bar]	postponed							
10	Re-install lights endcap A	1 day				[blue bar]	Enrique, Davy						
11	remove RIF C vessels	1 day			[blue bar]	RIF team							
12	extract RIF A chambers and drift boxes	2.5 days				[blue bar]		RIF team					
13	Prepare TPC opening C (?)	0.5 days				[blue bar]	Jean, Bernard						
14	Open TPC side C (?)	2 days				[blue bar]		TPC team					
15	Repas de fin d'année	0.5 days						[blue bar]	toute l'equipe				

Problems:



French customs has still not given authorisation to pass material through France. Solution must be found this week! -> Hübner/Cashmore/Stassinakis.

Electronics pool still not able to take back equipment. Removal of pool electronics from SU8 is responsibility of pool.

....

<http://delonline.cern.ch/~augustinus/dismantling/pool/welcome.html>

We request to subtract this equipment from our pool rental list with immediate effect.

In order to liberate the very limited space in the UX85 cavern and the SX85 hall, we were forced to store the palettes in the hall SU8, which houses cooling and ventilation installations and is under the responsibility of the ST/CV group. No formal agreement exists for this temporary storage.

....


We consider it as the responsibility of the EP pool to remove the electronics from this hall as soon as possible. We decline any responsibility for future theft or damage of electronics equipment while stored in this hall.

.....

Planning for this week (week 2/2001)



ID	Task Name	Sun 7 Jan	Mon 8 Jan	Tue 9 Jan	Wed 10 Jan	Thu 11 Jan	Fri 12 Jan	Sat 13 Jan	Sun 14 Jan	Mon 15 Jan
		S	M	T	W	T	F	S	S	M
1	remove RIF A drift boxes		[Task Bar]							
2	remove FCB side C			[Task Bar]						
3	remove RIF A vessels				[Task Bar]					
4	remove FCB side A						[Task Bar]			
5	remove FEMC electronics		[Task Bar]							
6	remove FEMC modules side C					[Task Bar]				
7	remove MUB lower peripheral chambers			[Task Bar]						
8	remove RIB dist column		[Task Bar]							
9	remove water tubes B4 / B3			[Task Bar]						
10	remove passerelle B4-Barrel			[Task Bar]						
11	remove B4,B3									[Task Bar]

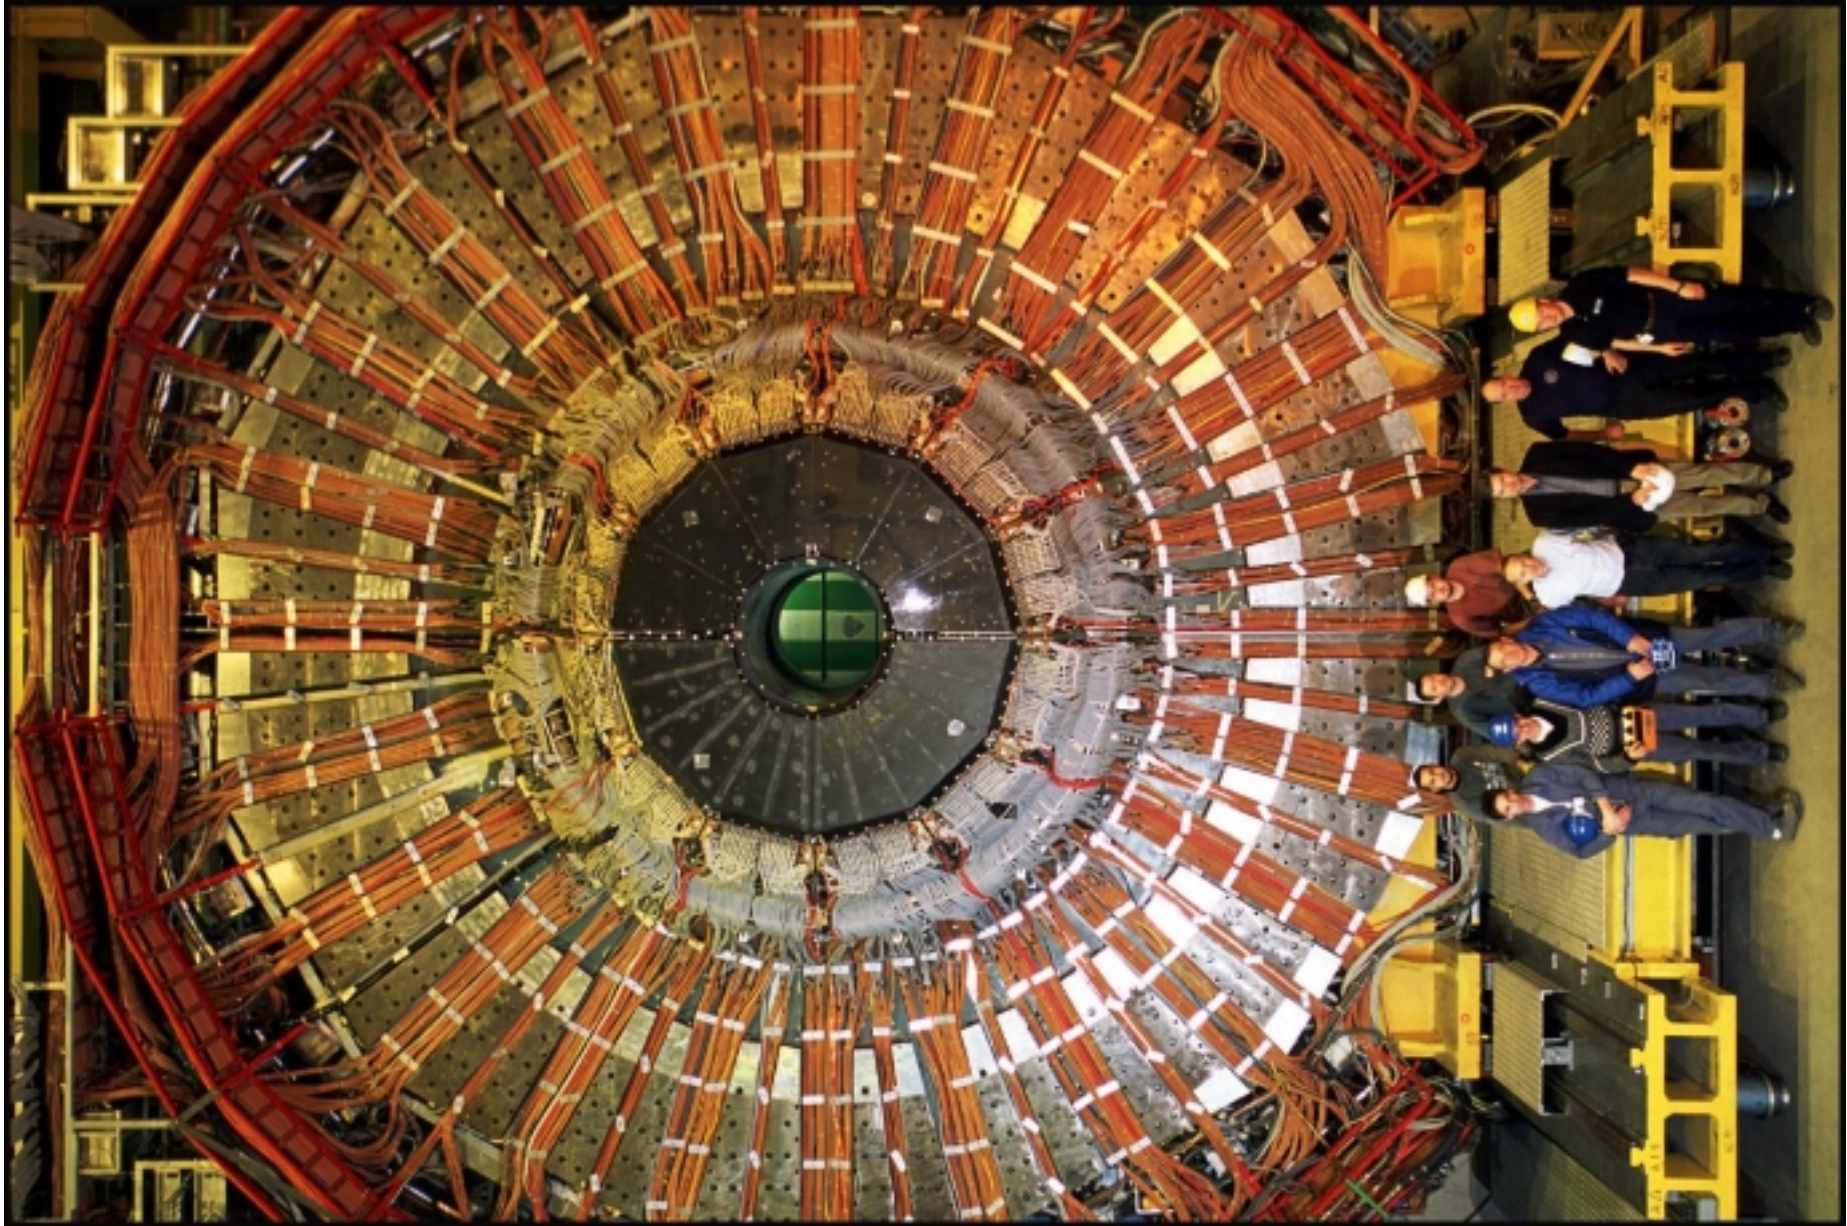

5th DDM, 08-01-2001, C. Joram
