



8th DELPHI Dismantling Meeting


Monday, 29 Jan 2001, 8:15 h

Progress during week 04/2001

Planning for week 05/2001

A.O.B

Progress during last week (week 4/2001)

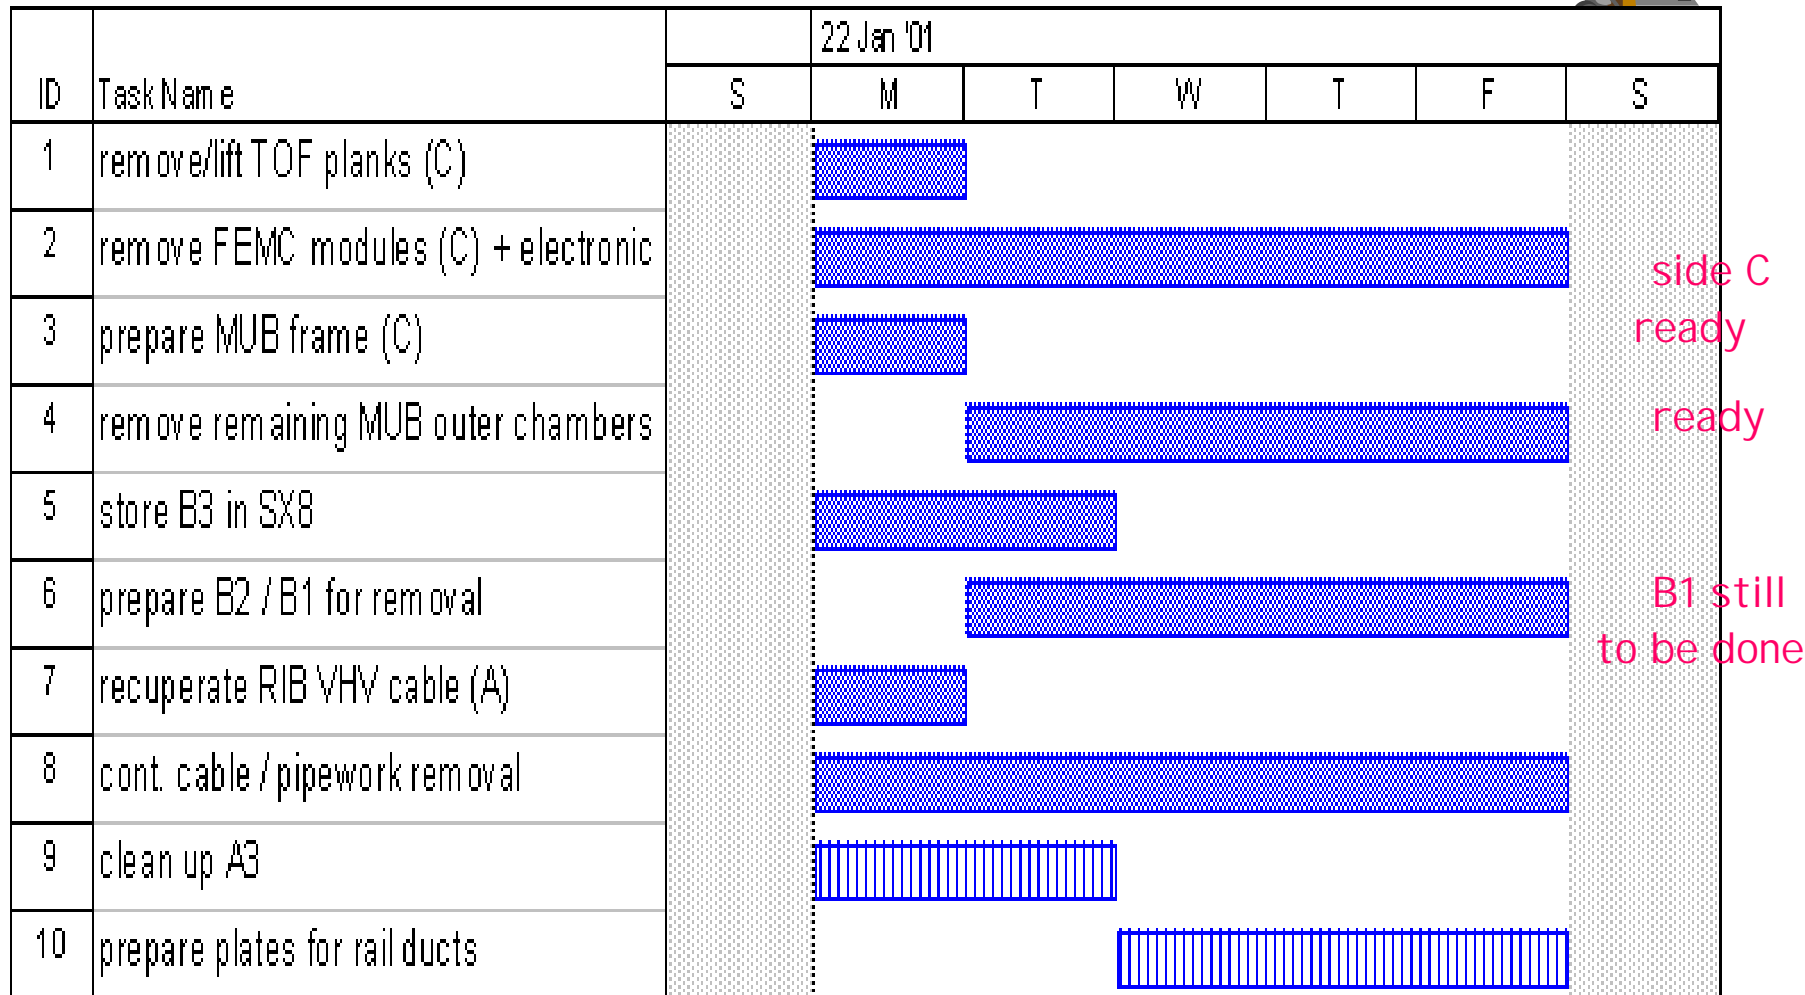

VERY GOOD PROGRESS !

Problems ?

Messieurs,



Je viens d'avoir un entretien téléphonique avec Monsieur Gérardot, remplaçant du Directeur adjoint des Douanes du Léman, qui m'a informé que les procédures douanières seront signées par le Directeur régional ce lundi 29 janvier 2001 et que les activités pourront commencer à cette date.

Toutefois, je propose de prendre contact avec le Directeur adjoint des Douanes du Léman dès lundi matin pour demander confirmation de cette nouvelle. Je vous informerai immédiatement de sa réponse.

Bon weekend,

--

Friedemann Eder
Relations avec les Pays-hôtes
Host States Relations

Planning for this week (week 5/2001)



		28 Jan '01						
ID	Task Name	S	M	T	W	T	F	S
1	rem ove gas bottle in B1		■					
2	FEMC side A		■	■	■	■	■	■
3	Lift bar. B2 to SX		■					
4	Prep. B2 for transport/rem. Racks			■	■	■	■	
5	Transport B2 -> point 2 (L3)						■	
6	rem ove balcon B1 front		■					
7	rem ove balcon B1 back			■				
8	place B1 on platform						■	
9	close TPC endplate (C)		■	■	■	■	■	■
10	rem ove gas racks A3		■	■	■	■	■	■

Russian colleagues will construct frames for HOF counters in SX workshop. HOF dismantling starts on 19 Feb. -> CORAL project.
